


Phasing Preferred Schematic



- ### Programs Relocated Off-Site
- LABBB MS → perm. 2018
 - Daycare → temp. Hardy
 - Preschool → temp. Parmenter
 - Comptroller → perm. Town Hall
 - Town Facilities → perm. DPW
 - LABBB HS → ?
 - District → ?
 - Payroll → ?
 - Town IT → ?

Phasing Preferred Schematic

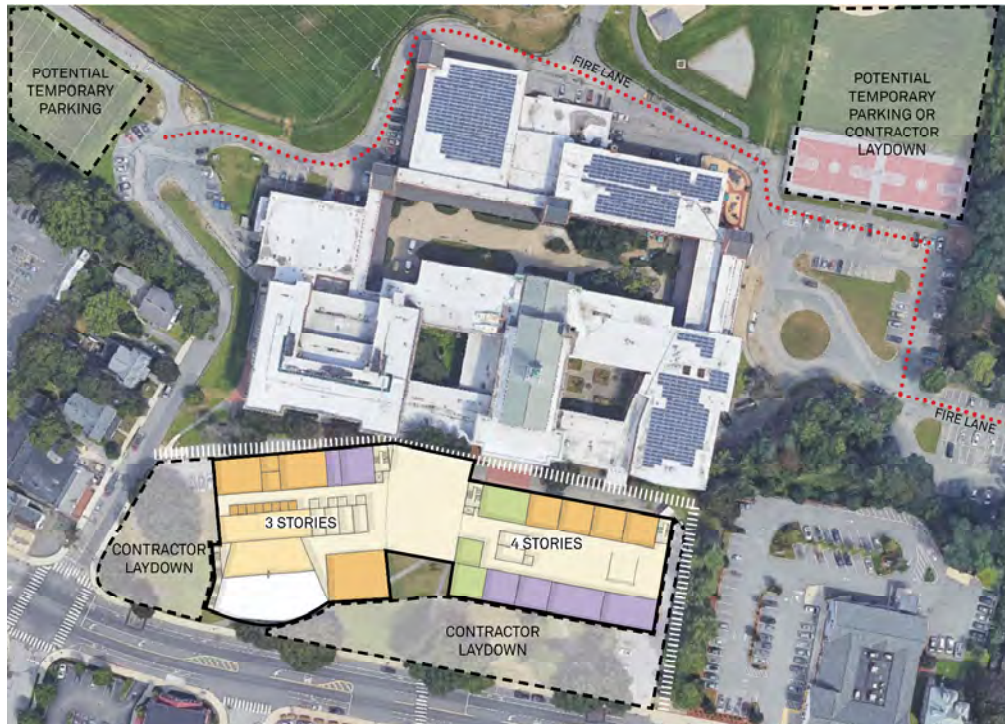

Phase 1 Temp / Relocations
Existing school remains intact
Temporary parking needed


July 2020
18 months

January 2022

Phase 1

- Hazmat / Demo
- Construction / Move In

Phasing Preferred Schematic

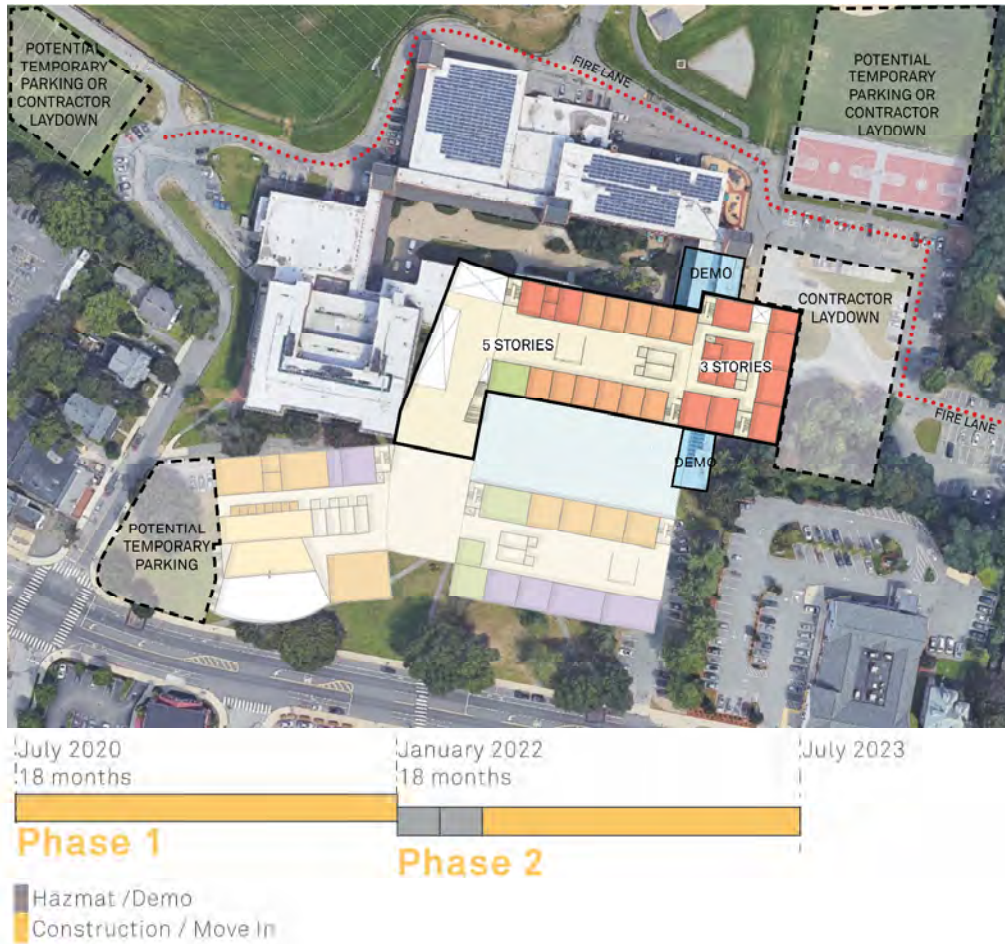

Phase 2 Temp / Relocations

Cafeteria → Blue Gym


Kitchen → food delivery

Media Center → Old Hall,
Fusco 3rd Floor CR's

Phasing Preferred Schematic




Phase 3 Temp / Relocations
None – Red Gym/lockers remain in use





Phasing Preferred Schematic

Fully Occupied September 2024

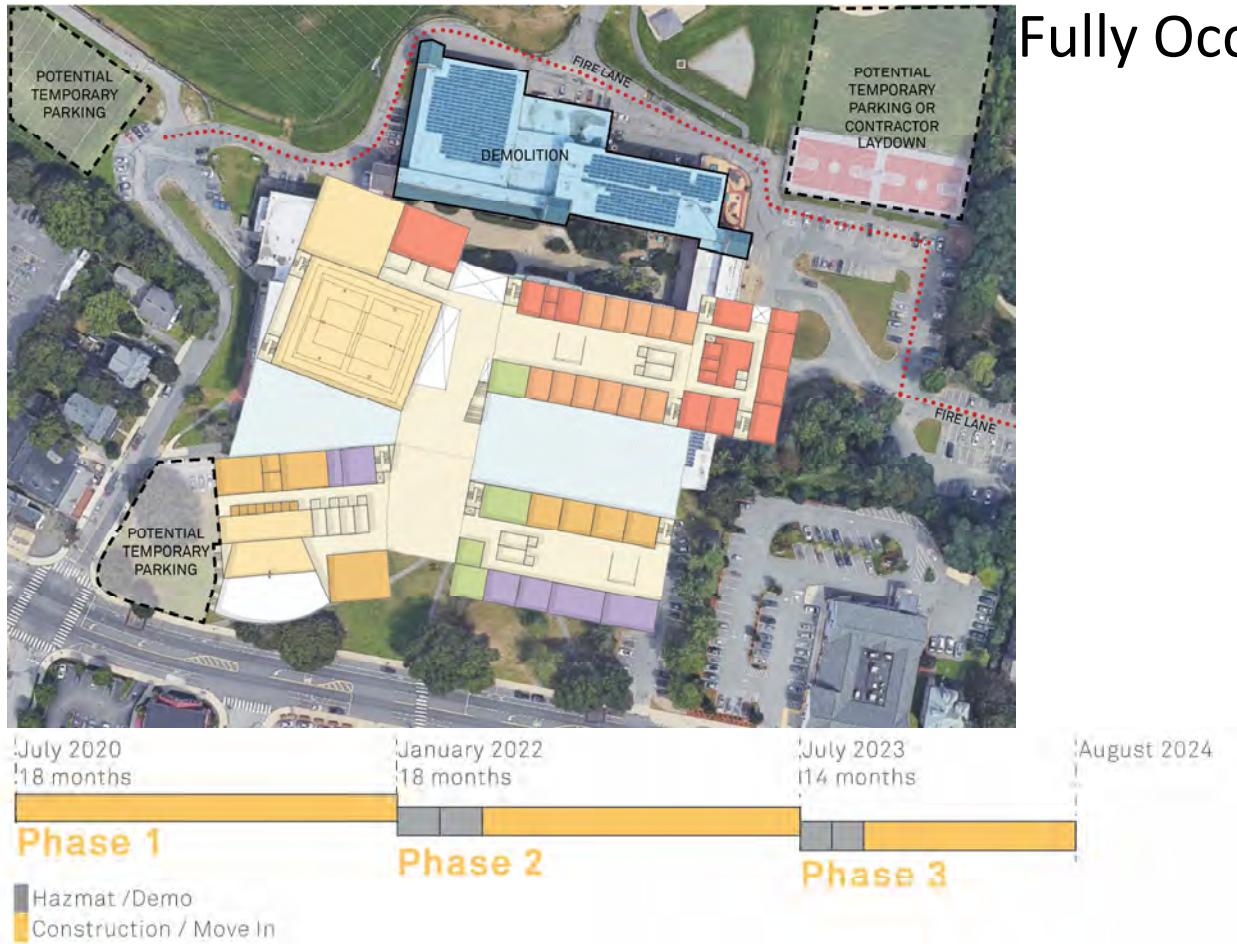

Phasing Preferred Schematic

Fully Occupied September 2024

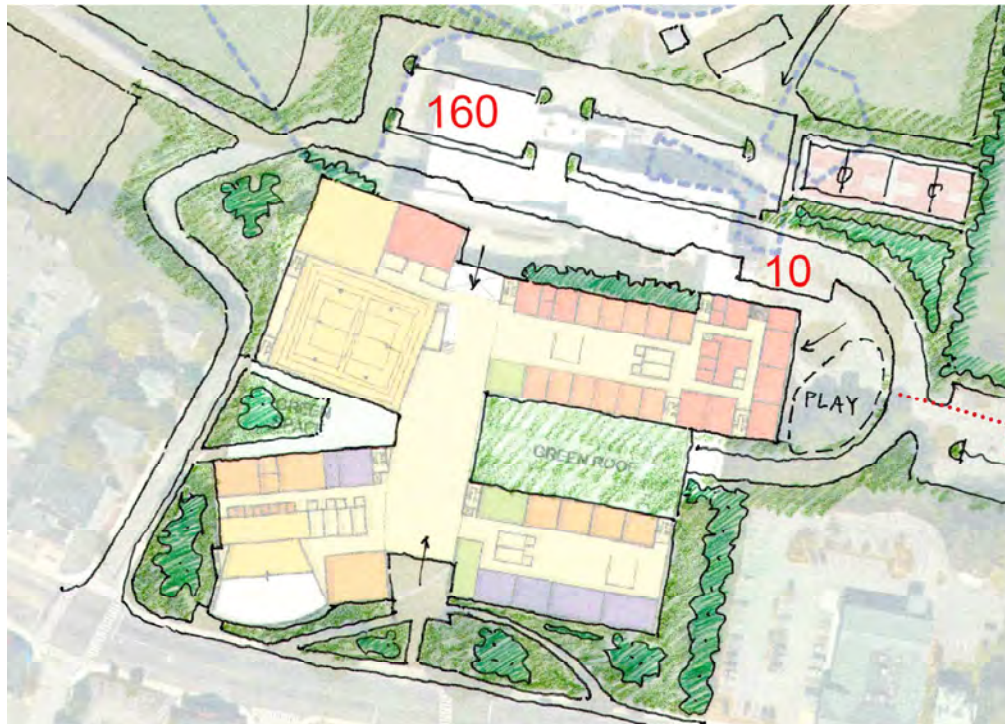

April 2025
Completion
4 years 10 mo
